

**NOTICE OF SPECIAL MEETING
OF THE
SOUTH ORANGE COUNTY WASTEWATER AUTHORITY
PROJECT COMMITTEE 2**

December 7, 2023

9:30 a.m.

(or immediately following the Regular Board meeting)

NOTICE IS HEREBY GIVEN that a Special Meeting of the South Orange County Wastewater Authority (SOCWA) Project Committee 2 was called to be held on **December 7, 2023, at 9:30 a.m. (or immediately following the Regular Board meeting)**. SOCWA staff will be present and conducting the meeting at the SOCWA Administrative Office located at 34156 Del Obispo Street, Dana Point, California.

THE SOCWA MEETING ROOM IS WHEELCHAIR ACCESSIBLE. IF YOU REQUIRE ANY SPECIAL DISABILITY RELATED ACCOMMODATIONS, PLEASE CONTACT THE SOUTH ORANGE COUNTY WASTEWATER AUTHORITY SECRETARY'S OFFICE AT (949) 234-5452 AT LEAST TWENTY-FOUR (24) HOURS PRIOR TO THE SCHEDULED MEETING TO REQUEST SUCH ACCOMMODATIONS. THIS AGENDA CAN BE OBTAINED IN ALTERNATE FORMAT UPON REQUEST TO THE SOUTH ORANGE COUNTY WASTEWATER AUTHORITY'S SECRETARY AT LEAST TWENTY-FOUR (24) HOURS PRIOR TO THE SCHEDULED MEETING. MEMBERS OF THE PUBLIC HAVE THE OPTION TO PARTICIPATE IN AND MAY JOIN THE MEETING REMOTELY VIA VIDEO CONFERENCE FOR VISUAL INFORMATION ONLY (USE ZOOM LINK BELOW) AND BY TELECONFERENCE FOR AUDIO PARTICIPATION (USE PHONE NUMBERS BELOW). THIS IS A PHONE-CALL MEETING AND NOT A WEB-CAST MEETING, SO PLEASE REFER TO AGENDA MATERIALS AS POSTED ON THE WEBSITE AT WWW.SOCWA.COM. ON YOUR REQUEST, EVERY EFFORT WILL BE MADE TO ACCOMMODATE PARTICIPATION. FOR PARTIES PARTICIPATING REMOTELY, PUBLIC COMMENTS WILL BE TAKEN DURING THE MEETING FOR ORAL COMMUNICATION IN ADDITION TO PUBLIC COMMENTS RECEIVED BY PARTIES PARTICIPATING IN PERSON. COMMENTS MAY BE SUBMITTED PRIOR TO THE MEETING VIA EMAIL TO ASSISTANT SECRETARY DANITA HIRSH AT DHIRSH@SOCWA.COM WITH THE SUBJECT LINE "REQUEST TO PROVIDE PUBLIC COMMENT." IN THE EMAIL, PLEASE INCLUDE YOUR NAME, THE ITEM YOU WISH TO SPEAK ABOUT, AND THE TELEPHONE NUMBER YOU WILL BE CALLING FROM SO THAT THE COORDINATOR CAN UN-MUTE YOUR LINE WHEN YOU ARE CALLED UPON TO SPEAK. THOSE MAKING PUBLIC COMMENT REQUESTS REMOTELY VIA TELEPHONE IN REAL-TIME WILL BE ASKED TO PROVIDE YOUR NAME, THE ITEM YOU WISH TO SPEAK ABOUT, AND THE TELEPHONE NUMBER THAT YOU ARE CALLING FROM SO THE COORDINATOR CAN UN-MUTE YOUR LINE WHEN YOU ARE CALLED UPON TO SPEAK. ONCE THE MEETING HAS COMMENCED, THE CHAIR WILL INVITE YOU TO SPEAK AND ASK THE COORDINATOR TO UN-MUTE YOUR LINE AT THE APPROPRIATE TIME.

AGENDA ATTACHMENTS AND OTHER WRITINGS THAT ARE DISCLOSABLE PUBLIC RECORDS DISTRIBUTED TO ALL, OR A MAJORITY OF, THE MEMBERS OF THE SOUTH ORANGE COUNTY WASTEWATER AUTHORITY PROJECT COMMITTEE 2 IN CONNECTION WITH A MATTER SUBJECT FOR DISCUSSION OR CONSIDERATION AT AN OPEN MEETING OF THE PROJECT COMMITTEE 2 ARE AVAILABLE FOR PUBLIC INSPECTION IN THE AUTHORITY ADMINISTRATIVE OFFICE LOCATED AT 34156 DEL OBISPO STREET, DANA POINT, CA ("AUTHORITY OFFICE") OR BY PHONE REQUEST MADE TO THE AUTHORITY OFFICE AT 949-234-5452. IF SUCH WRITINGS ARE DISTRIBUTED TO MEMBERS OF THE PROJECT COMMITTEE 2 LESS THAN TWENTY-FOUR (24) HOURS PRIOR TO THE MEETING, THEY WILL BE AVAILABLE IN THE RECEPTION AREA OF THE AUTHORITY OFFICE AT THE SAME TIME AS THEY ARE DISTRIBUTED TO THE PROJECT COMMITTEE 2 AND SENT TO ANY REMOTE PARTICIPANTS REQUESTING EMAIL DELIVERY OR POSTED ON SOCWA'S WEBSITE. IF SUCH WRITINGS ARE DISTRIBUTED IMMEDIATELY PRIOR TO, OR DURING, THE MEETING, THEY WILL BE AVAILABLE IN THE MEETING ROOM OR IMMEDIATELY UPON VERBAL REQUEST TO BE DELIVERED VIA EMAIL TO REQUESTING PARTIES PARTICIPATING REMOTELY.

**THE PUBLIC MAY PARTICIPATE REMOTELY BY VIRTUAL MEANS. FOR AUDIO OF MEETING USE
THE CALL IN PHONE NUMBERS BELOW AND FOR VIDEO USE THE ZOOM LINK BELOW.**

Join Zoom Meeting

<https://socwa.zoom.us/>

Meeting ID: 857 4457 1917

Passcode: 777707

Dial by your location:

+1 669 900 6833 US (San Jose) +1 253 215 8782 US (Tacoma)
+1 346 248 7799 US (Houston) +1 312 626 6799 US (Chicago)

Find your local number: <https://socwa.zoom.us/j/kcarzMVgMP>

AGENDA

1. Call Meeting to Order

2. Public Comments

THOSE WISHING TO ADDRESS THE ENGINEERING COMMITTEE ON ANY ITEM LISTED ON THE AGENDA WILL BE REQUESTED TO IDENTIFY AT THE OPENING OF THE MEETING AND PRIOR TO THE CLOSE OF THE MEETING. THE AUTHORITY REQUESTS THAT YOU STATE YOUR NAME WHEN MAKING THE REQUEST IN ORDER THAT YOUR NAME MAY BE CALLED TO SPEAK ON THE ITEM OF INTEREST. THE CHAIR OF THE MEETING WILL RECOGNIZE SPEAKERS FOR COMMENT AND GENERAL MEETING DECORUM SHOULD BE OBSERVED IN ORDER THAT SPEAKERS ARE NOT TALKING OVER EACH OTHER DURING THE CALL.

3. Closed Session

A. Closed Session Conference with Legal Counsel – Anticipated Litigation (Gov. Code 54956.9(d)(2)) – One potential matter

4. Open Session

A. Report out of Closed Session

B. Capital Improvement Construction Projects Progress and Change Orders to Olsson Construction [Project Committee No. 2]

Recommended Action: Staff recommends that the PC 2 Board of Directors i) approve Change Orders 73 through 80 for \$482,878.33 to Olsson Construction for the JBL Package B project and ii) authorize the Acting General Manager to release retention funds to Olsson Construction for the JBL Package B Project of up to \$931,343.41, withholding funds for estimated liquidated damages, estimated legal fees, and pending change orders.

Adjournment

I hereby certify that the foregoing Notice was personally emailed or mailed to each member of the SOCWA Project Committee 2 at least 24 hours prior to the scheduled time of the Special Meeting referred to above.

I hereby certify that the foregoing Notice was posted at least 24 hours prior to the time of the above-referenced Project Committee meeting at the usual agenda posting location of the South Orange County Wastewater Authority and at www.socwa.com.

Dated this 4th day of December 2023.



Danita Hirsh, Assistant Secretary
SOUTH ORANGE COUNTY WASTEWATER AUTHORITY

Agenda Item

4.B.

PC 2 Committee Meeting

Meeting Date: December 7, 2023

TO: PC 2 Board of Directors

FROM: Jim Burror, Acting General Manager/Director of Operations

STAFF CONTACTS: Roni Grant, Associate Engineer

SUBJECT: Capital Improvement Construction Projects Progress and Change Orders to Olsson Construction [Project Committee No. 2]

Overview

This agenda item provides an update on projects in construction, including any change orders. Attached are the updated CIP reports.

Project Updates

JBL Package B

The project is complete, and Staff continue to work with the Construction Management team to close out all outstanding items. There are eight new change orders for this project totaling \$482,878.33:

- Change Order 73 for \$67,278.13
- Change Order 74 for \$82,810.21
- Change Order 75 for \$6,537.01
- Change Order 76 for \$39,052.96
- Change Order 77 for \$41,697.76
- Change Order 78 for \$57,928.56
- Change Order 79 for \$79,117.65
- Change Order 80 for \$108,456.05

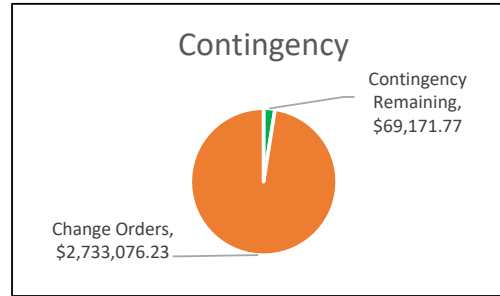
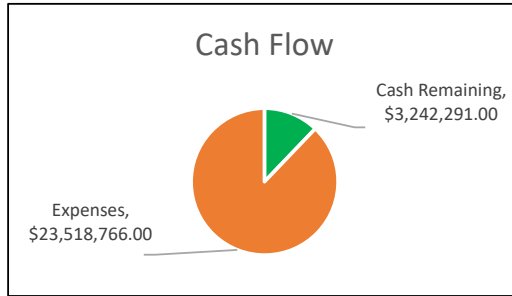
Recommended Action: Staff recommends that the PC 2 Board of Directors i) approve Change Orders 73 through 80 for \$482,878.33 to Olsson Construction for the JBL Package B project and ii) authorize the Acting General Manager to release retention funds to Olsson Construction for the JBL Package B Project of up to \$931,343.41, withholding funds for estimated liquidated damages, estimated legal fees, and pending change orders.

Project Financial Status

Project Committee	2
Project Name	Package B
Project Description	Plant 1 basin repairs, DAF rehabilitation, Energy Building seismic retrofit and minor rehabilitation, Digester 4 rehabilitation

Data Last Updated

October 30, 2023

**Cash Flow**

Collected	\$ 26,761,057.00
Expenses	\$ 23,518,766.00

Project Completion

Schedule	100%
Budget	97%

Contracts

Company	PO No.	Original	Change Orders*	Amendments	Total	Invoiced
Olsson	13497	\$ 17,325,000.00	\$ 1,784,746.22		\$ 19,109,746.22	\$ 18,626,868.23
Butier	13647	\$ 895,727.00		\$ 1,005,251.00	\$ 1,900,978.00	\$1,898,574.50
Carollo	13616	\$ 846,528.00		\$ 616,037.00	\$ 1,462,565.00	\$1,406,941.05
TetraTech	13605	\$ 94,000.00		\$ -	\$ 94,000.00	\$ 93,884.70
Ninyo & Moore	14279	\$ 49,399.00		\$ 30,000.00	\$ 79,399.00	\$ 50,166.27
ADS Environmental	16452	\$ 107,200.00	\$ -		\$ 107,200.00	\$ 61,875.00
Dudek	17401	\$ 48,360.00		\$ -	\$ 48,360.00	\$ 42,160.00
		\$ 19,366,214.00	\$ 1,784,746.22	\$ 1,651,288.00	\$ 22,802,248.22	\$ 22,180,469.75

*Values include change orders to be reviewed by Engineering Committee and deductive change orders

Contingency

Area	Project Code	Amount **	Change Orders	Total Remaining	Percent Used
Liquids	3220-000	\$ 1,219,679.00	\$ 1,194,892.44	\$ 24,786.56	98.0%
Common	3231-000	\$ 38,120.00	\$ 9,842.77	\$ 28,277.23	25.8%
Solids	3287-000	\$ 1,544,449.00	\$ 1,528,341.02	\$ 16,107.98	99.0%
		\$ 2,802,248.00	\$ 2,733,076.23	\$ 69,171.77	97.5%

** Amount reflects contingency for Construction Contracts only and direct Board change orders approval.

Change Order No	MNWD	SCWD	SMWD	\$ Amount
73	\$14,545.53	\$13,455.63	\$39,276.97	\$67,278.13
74	\$17,903.57	\$16,562.04	\$48,344.60	\$82,810.21
75	\$1,460.97	\$1,596.54	\$3,479.52	\$6,537.03
76	\$9,013.42	\$11,262.87	\$18,776.66	\$39,052.95
77	\$9,623.84	\$12,025.63	\$20,048.28	\$41,697.75
78	\$13,369.91	\$16,706.60	\$27,852.05	\$57,928.56
79	\$18,260.35	\$22,817.53	\$38,039.77	\$79,117.65
80	\$25,031.66	\$31,278.72	\$52,145.67	\$108,456.05
Grand Total	\$109,209.25	\$125,705.56	\$247,963.52	\$482,878.33

Change Orders and Amendments

Change Order No.	Vendor Name	Project ID	Description	Status Date	Days	Amount
Within Contingency, to be reviewed by Engineering Committee						\$ 482,878.33
73	Olsson	3287-000	TWAS/DAFT Area Modifications	9/27/2023		\$ 67,278.13
74	Olsson	3287-000	Digester Area Ductbank Conflicts and Additional Work	9/27/2023		\$ 82,810.21
75	Olsson	3231-000	Lab Building Footing Demolition	9/27/2023		\$ 6,537.01
76	Olsson	3220-000	Plant 1 Additional Repair and Modification	9/27/2023		\$ 39,052.96
77	Olsson	3220-000	Plant 2 Additional Repair and Modification	9/27/2023		\$ 41,697.76
78	Olsson	3220-000	Aluminum Kickplate at Aeration Tanks	9/27/2023		\$ 57,928.56
79	Olsson	3220-000	Phase 1 Bypass Pumping	9/27/2023		\$ 79,117.65
80	Olsson	3220-000	Phases 2 and 3 Bypass Pumping	9/27/2023		\$ 108,456.05
Approved by Board of Directors (Amendments)					191	\$ 1,318,583.14
1	Olsson	3287-000	Addition of Loop Piping to the Existing Hot Water Lines Adjacent to Digester 3	12/12/2019	0	\$ 4,725.00

2	Olsson	3287-000	Asbestos Gaskets in Boiler hazardous disposal	6/4/2020	0	\$ 6,343.10
3	Olsson	3287-000	Add Analog Infrastructure and Cabling	6/4/2020	11	\$ 37,969.60
4	Olsson	3287-000	Digester 4 Coating Additional Sealant	6/4/2020	3	\$ 24,001.54
5	Olsson	3220-000	Valve Handwheel Ergonomic extension	8/6/2020	28	\$ 16,370.30
6	Olsson	3287-000	Change to DeZurik Plug Valves to match existing	8/6/2020	90	\$ 41,993.87
7	Olsson	3287-000	Digester 4 Additional Concrete Repair	8/6/2020	3	\$ 7,412.74
8	Olsson	3287-000	Repair Existing Damaged Electrical Box	8/6/2020	0	\$ (1,829.00)
9	Olsson	3220-000	Change the Telescoping Valve Boxes and Piping from Carbon Steel to Stainless Steel	8/6/2020	0	\$ 18,677.63
10	Olsson	3287-000	Duct bank J Interferences	12/17/2020	18	\$ 73,639.42
11	Olsson	3220-000	Blasting of Existing Influent Pipe Spools	12/17/2020	5	\$ 20,868.52
12	Olsson	3220-000	Duct bank K Interferences	12/17/2020	0	\$ 15,567.08
13	Olsson	3287-000	Digester 3/4 PLC Relocation	12/17/2020	14	\$ 41,367.51
14	Olsson	3287-000	Digester 4 Additional Tank Repair	12/17/2020	18	\$ 33,642.75
15	Olsson	3220-000	Duct bank O Interferences	12/17/2020	0	\$ 1,686.88
16	Olsson	3287-000	Digester 3/4 Control Building Roof Replacement	2/4/2021	0	\$ 42,780.00

17	Olsson	3287-000	MCC-D1 Modifications due to Change in Motor Size	5/6/2021	0	\$ 34,392.02
18	Olsson	3287-000	Integrator Additional Site Visits	5/6/2021	0	\$ 7,571.97
19	Olsson	3287-000	Multi-zone air conditioning unit in the Cogen MCC Room and Office	6/3/2021	0	\$ 29,417.20
20	Olsson	3220-000	Overhead Walkway Removal at Plant 1 Secondary Basins 5 through 9	6/3/2021	0	\$ 62,113.50
21	Olsson	3287-000	Cogeneration PLC Modifications and Integration	6/3/2021	0	\$ 42,922.67
22	Olsson	3220-000	Plant 1 Secondary Basins UV Rated Wear Strips	9/2/2021	0	\$ 28,965.33
23	Olsson	3287-000	MCC-F1 Design Change	9/2/2021		\$ 481,290.42
24	Olsson	3287-000	DAF 2 Investigation Work and Inspection Blast	10/7/2021		\$ 67,838.71
25	Olsson	3287-000	New Fiber Conduit in West Blower Building	10/7/2021		\$ 4,957.71
26	Olsson	3220-000	Plant 1 Primary Basin Conduit Obstruction	10/7/2021		\$ 8,444.20
27	Olsson	3220-000	Plant 1 Influent Channel Additional Coating between Primary Basins 5 and 6	10/7/2021		\$ 15,469.98
28	Olsson	3287-000	MCC-F1 Lighting Changes	10/7/2021		\$ 7,843.04
29	Olsson	3287-000	Digester 3 Ground Rod	10/14/2021		\$ 7,269.16
30	Olsson	3220-000	New Fiber Conduits at East Electrical and Storm Water Buildings	10/14/2021		\$ 8,045.43
31	Olsson	3220-000	Plant 2 Primary Influent Channel Repair Credit	12/9/2021		\$ (15,903.00)

32	Olsson	3220-000	Plant 1 and 2 Telescoping Valve Pipe Supports	12/9/2021		\$ 6,132.27
33	Olsson	3287-000	4" Gas Line Routing Modifications	12/9/2021		\$ 18,146.07
34	Olsson	3287-000	Gas Mixer Conduit Conflict	12/9/2021		\$ 12,383.89
35	Olsson	3220-000	P1 Primary Tanks 5 and 6 Temporary Power	3/10/2022		\$ 7,256.05
36	Olsson	3220-000	P1 Primary Tanks Skimmers Starter Modification	3/10/2022		\$ 45,374.13
37	Olsson	3220-000	P1 Primary Tanks Hopper Wall Coating	3/10/2022		\$ 34,505.41
38	Olsson	3220-000	P1 Effluent Channel Conduit Conflict	3/10/2022		\$ 9,274.98
39	Olsson	3220-000	P1 Primary Tanks Torque Limit Switch	3/10/2022		\$ 7,149.86
40	Olsson	3287-000	Multi-zone air conditioning unit in the Cogen MCC Room and Office	3/10/2022		\$ (2,309.09)
41	Olsson	3287-000	DAFT 2 Repair	3/10/2022		\$ 59,403.53
42	Olsson	3287-000	Digesters 1 and 2 Heat Exchanger Layout Reconfiguration Electrical	6/2/2022	1	\$ 12,885.18
43	Olsson	3287-000	Digester 3 Heat Exchanger Hot Water Loop Tie-In	6/2/2022		\$ 2,774.58
44	Olsson	3220-000	Plant 1 Primary Basin 1 Shutdown Repair Work	6/2/2022		\$ 1,009.86
45	Olsson	3287-000	Replace Compressor Line and Valve at Digester 4	6/2/2022		\$ 10,762.85
46	Olsson	3220-000	Plant 2 Influent Gates Removal and Concrete Demo	6/2/2022		\$ 5,389.66

47	Olsson	3287-000	DAFT 2 Launder Support Detail	6/9/2022		\$ 45,682.30
48	Olsson	3220-000	Plant 1 Primary Basins 1, 2, 5 and 6 Coating Removal	6/9/2022		\$ 111,101.16
49	Olsson	3220-000	Plant 1 Primary Basins 1, 2, 5 and 6 Existing Equipment Removal and Reinstallation	6/9/2022		\$ 71,864.17
50	Olsson	3287-000	Digester Mixing Pumps Control Programming Change	8/4/2022		\$ 4,397.77
51	Olsson	3220-000	Plant 1 Primary Basins Skimmers I/O Connection and Programming Change	8/4/2022		\$ 14,237.83
52	Olsson	3287-000	Fiber Patch Cables to Connect the Centrifuge PLC to the Centrifuge Patch Panel	8/4/2022		\$ 3,755.90
53	Olsson	3220-000	Plant 1 Primary Basins 3 and 4 Coating Removal	8/4/2022		\$ 43,222.24
54	Olsson	3220-000	Plant 1 Secondary Basins Concrete Structural and Basins 2 and 3 Drive Plate Rework	8/4/2022		\$ 20,860.16
55	Olsson	3220-000	Plant 2 Primary Basins Repair and Rehab of Head-Shaft Bearings	8/4/2022		\$ 4,618.44
56	Olsson	3231-000	Board SOCWA Front Office with Plywood to Cover Windows	8/4/2022		\$ 3,305.76
57	Olsson	3220-000	Seal the Openings at Plant 1 Primary Influent and Effluent Channels	8/4/2022		\$ 25,491.03

58	Olsson	3220-000	Plant 1 Primary Basins 3 and 4 Existing Equipment Removal and Reinstallation	9/1/2022		\$ 26,498.32
59	Olsson	3220-000	Plant 1 Secondary Basins Existing Embedded Metal Plates	9/1/2022		\$ 4,290.48
60	Olsson	3220-000	Plant 2 Primary Baffle Frame Replacement	9/1/2022		\$ 18,291.57
61	Olsson	3287-000	Digester hatch connection, temperature gauge adjustment, and potholing	11/3/2022		\$ 9,971.62
62	Olsson	3220-000	Plant 1 Primary and Secondary Basins crack injection, concrete repair, channel cleaning, solids removal	11/3/2022		\$ 146,734.55
63	Olsson	3287-000	Boiler Room Modifications	12/8/2022		\$ 14,797.83
64	Olsson	3287-000	DAFT 1 Repair	12/8/2022		\$ 66,992.33
65	Olsson	3220-000	Secondary Clarifier Telescoping Valve Modifications (Design Error)	12/8/2022		\$ 32,709.94
66	Olsson	3287-000	Digester Control Buildings Modifications	2/2/2023		\$ 9,746.81
67	Olsson	3220-000	Plant 1 and 2 Field Obstructions	2/2/2023		\$ 8,871.74
68	Olsson	3287-000	MCC-F1 Site Modifications	2/2/2023		\$ 57,233.12
69	Olsson	3287-000	DAFT and TWAS area additional slab modification and piping material change	2/2/2023		\$ 19,368.58
70	Olsson	3287-000	DAFT 1 Area Reconfiguration	3/2/2023		\$ 3,046.43

71	Olsson	3287-000	Digester 2 Hot Water Loop Change	3/2/2023		\$ 29,525.46
72	Olsson	3220-000	Plant 1 Seal Influent Channel Openings and Helical Drives Temporary Covers	4/6/2023		\$ 10,831.51
Deduct-Common	Olsson	3231-000	Energy Building Monorail System Descope (F1-F4)	8/4/2022		\$ (70,585.34)
Deduct-Liquids	Olsson	3220-000	Effluent Pump Station Descope (A1-A6)	8/4/2022		\$ (483,605.73)
Deduct-Solids	Olsson	3287-000	Energy Building Modifications Descope (G1-G2, & H1-H2)	8/4/2022		\$ (357,382.60)
HAL 01	Hallsten	3220-000	Cover Layout Modifications	8/4/2022		\$ 16,715.25
Approved by Board of Directors (Amendments)						\$ 1,651,288.00
1CM Common	Butier	3231-000	CM Change Order No. 1	7/13/2021		\$ 48,995.00
1CM Liquids	Butier	3220-000	CM Change Order No. 1	7/13/2021		\$ 294,125.00
1CM Solids	Butier	3287-000	CM Change Order No. 1	7/13/2021		\$ 269,595.00
1ESDC Common	Carollo	3231-000	ESDC Change Order No. 1	6/3/2021		\$ 18,210.00
1ESDC Liquids	Carollo	3220-000	ESDC Change Order No. 1	6/3/2021		\$ 109,256.00
1ESDC Solids	Carollo	3287-000	ESDC Change Order No. 1	6/3/2021		\$ 100,151.00
1G Common	Ninyo & Moore	3231-000	Geotechnical Services Change Order No. 1	2/3/2022		\$ 5,400.00
1G Liquids	Ninyo & Moore	3220-000	Geotechnical Services Change Order No. 1	2/3/2022		\$ 12,300.00
1G Solids	Ninyo & Moore	3287-000	Geotechnical Services Change Order No. 1	2/3/2022		\$ 12,300.00
2CM Liquids	Butier	3220-000	CM Change Order No 2	5/12/2022		\$ 196,268.00
2CM Solids	Butier	3287-000	CM Change Order No. 2	5/12/2022		\$ 196,268.00

2ESDC Common	Carollo	3231-000	ESDC Change Order No. 2	12/9/2021		\$ 11,075.00
2ESDC Liquids	Carollo	3220-000	ESDC Change Order No. 2	12/9/2021		\$ 196,440.00
2ESDC Solids	Carollo	3287-000	ESDC Change Order No. 2	12/9/2021		\$ 180,905.00
Grand Total					191	\$ 3,452,749.47
